Activity ID	Activity Name	Original Duration	Start	Finish
DVT Relocatie Taxiway B & Construct Cc		306d	06-Jul-26	17-Sep-27
Preconstruction		64d	06-Jul-26	02-Oct-26
Submit Long Lead Items		1d	06-Jul-26	06-Jul-26
A1000	Submit Long Lead Items	1d	06-Jul-26	06-Jul-26
Review & Approve Long Lead Items		15d	07-Jul-26	27-Jul-26
A1010	Review & Approve Long Lead Items	15d	07-Jul-26	27-Jul-26
Procure Long Lead Items		60d	10-Jul-26	02-Oct-26
A1020	Procure Long Lead Items	60d	10-Jul-26	02-Oct-26
Construction		286d	03-Aug-26	17-Sep-27
A3030	Notice to Proceed	0d	03-Aug-26	
Phase 1		111d	03-Aug-26	12-Jan-27
P1000	Mobilization	0d	03-Aug-26	
P1010	Install SWPPP	2d	03-Aug-26	04-Aug-26
P1020	Relocate Primary Wind Cone & Segmented Ci	10d	03-Aug-26	17-Aug-26
P1030	Remove / Salvage Casper Rock	15d	03-Aug-26	24-Aug-26
P1040	Remove Edge Lights & Cans	10d	17-Aug-26	31-Aug-26
P1050	Mill AC (11")	7d	24-Aug-26	02-Sep-26
P1060	Precompaction of Fill Area	5d	24-Aug-26	31-Aug-26
P1070	Electrical Removals	7d	31-Aug-26	10-Sep-26
P1080	Remove Encased Duct Bank	5d	02-Sep-26	10-Sep-26
P1090	Unclassified Excavation	15d	10-Sep-26	01-Oct-26
P1100	Trench & Install New Conduit Runs	10d	01-Oct-26	15-Oct-26
P1110	Subgrade Preperation	15d	01-Oct-26	22-Oct-26
P1120	Lime Treat Subgrade	10d	22-Oct-26	05-Nov-26
P1130	Lime Cure	7d	05-Nov-26	12-Nov-26
P1140	Haul & Place P-209	15d	10-Nov-26	03-Dec-26
P1150	Install New Light Cans & Sign Bases	10d	12-Nov-26	30-Nov-26
P1160	Install 867E Junction Can	3d	30-Nov-26	03-Dec-26
P1170	Pull Wire	10d	03-Dec-26	17-Dec-26
P1180	Place P-401 Asphalt Mainline	6d	03-Dec-26	11-Dec-26
P1190	Place Back & Roll Casper Rock	15d	11-Dec-26	05-Jan-27
P1200	Install Lights & Guidance Signs	5d	05-Jan-27	12-Jan-27
Phase 2		114d	12-Jan-27	22-Jun-27
P2000	Install SWPPP	2d	12-Jan-27	14-Jan-27
P3200	Oblit Pavement Markings	2d	12-Jan-27	14-Jan-27
P2020	Remove / Salvage Casper Rock	15d	14-Jan-27	04-Feb-27
P2030	Remove Edge Lights & Cans	10d	14-Jan-27	28-Jan-27
P2060	Electrical Removals	7d	28-Jan-27	08-Feb-27
P2040	Mill AC (11")	7d	04-Feb-27	16-Feb-27
P2050	Precompaction of Fill Area	5d	04-Feb-27	11-Feb-27
P2070	Remove Encased Duct Bank	5d	16-Feb-27	23-Feb-27
P2080	Unclassified Excavation	15d	23-Feb-27	16-Mar-27
P2090	Trench & Install New Conduit Runs	10d	16-Mar-27	30-Mar-27
P2100	Subgrade Preperation	15d	16-Mar-27	06-Apr-27
P2110	Lime Treat Subgrade	10d	06-Apr-27	20-Apr-27
P2120	Lime Cure	7d	20-Apr-27	27-Apr-27
P2130	Haul & Place P-209	15d	26-Apr-27	14-May-27
P2140	Install New Light Cans & Sign Bases	10d	27-Apr-27	11-May-27
P2150	Install 867E Junction Can	3d	11-May-27	14-May-27
P2160	Pull Wire	10d	14-May-27	28-May-27

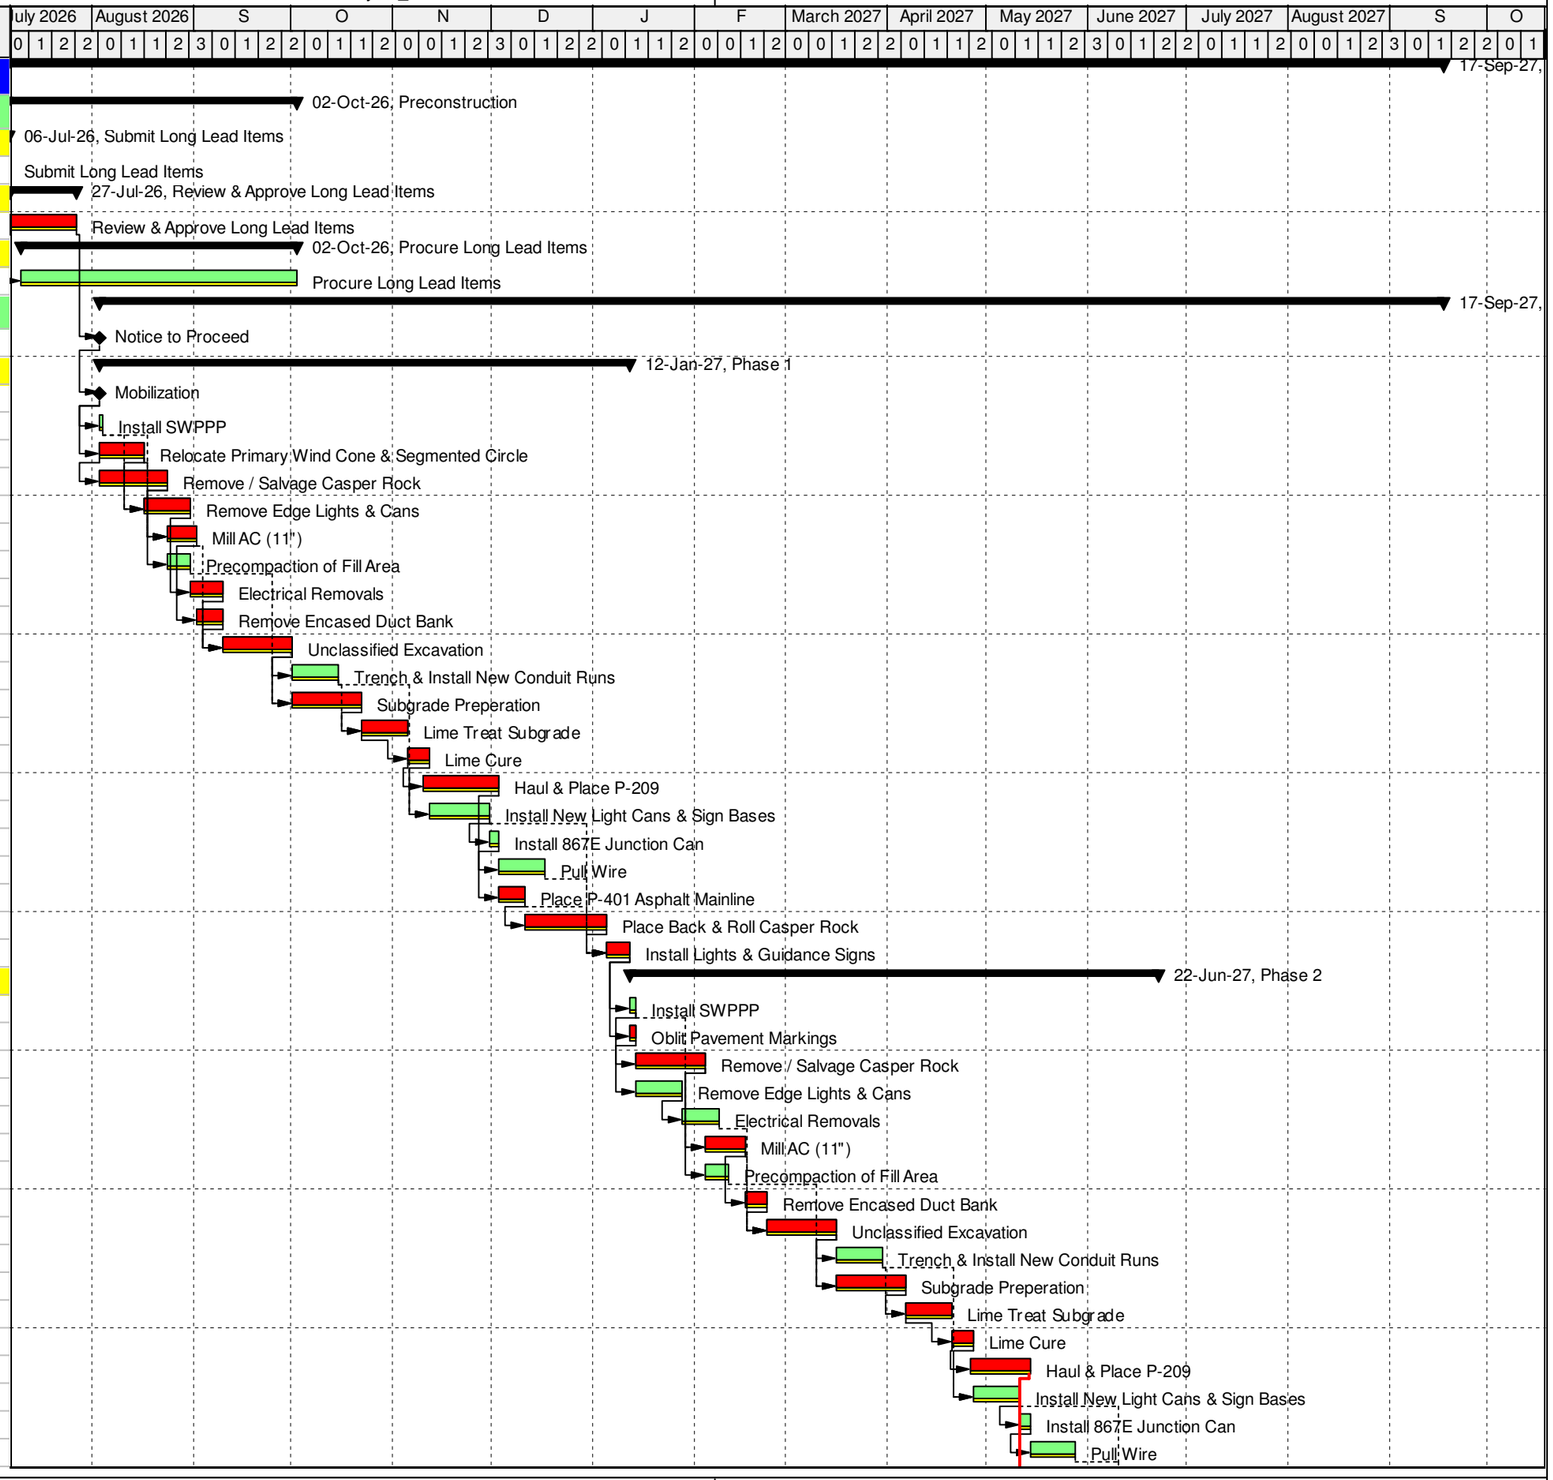

Project Baseline Bar | Actual Work | Remaining Work | Critical Remaining Work | Milestone | Summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Start	Finish
P2170	Place P-401 Asphalt Mainline	6d	17-May-27	24-May-27
P2180	Place Back & Roll Casper Rock	15d	25-May-27	15-Jun-27
P2190	Install Lights & Guidance Signs	5d	16-Jun-27	22-Jun-27
Phase 3		39d	23-Jun-27	17-Aug-27
P3020	Install SWPPP	1d	23-Jun-27	23-Jun-27
P3030	Mill AC	2d	24-Jun-27	25-Jun-27
P3010	Remove / Salvage Casper Rock	5d	28-Jun-27	02-Jul-27
P3040	Remove Concrete Encased Duct Bank	1d	28-Jun-27	28-Jun-27
P3050	Remove Edge Lights & Cans	1d	06-Jul-27	06-Jul-27
P3210	Precompaction of Fill Area	1d	06-Jul-27	06-Jul-27
P3060	Electrical Removals	1d	07-Jul-27	07-Jul-27
P3070	Unclassified Excavation	3d	08-Jul-27	12-Jul-27
P3080	Trench & Install New Conduit Runs	2d	13-Jul-27	14-Jul-27
P3090	Subgrade Preparation	3d	13-Jul-27	15-Jul-27
P3100	Lime Treat Subgrade	2d	16-Jul-27	19-Jul-27
P3110	Lime Cure	7d	21-Jul-27	27-Jul-27
P3120	Haul & Place P-209	3d	28-Jul-27	30-Jul-27
P3130	Place P-401 Asphalt	2d	02-Aug-27	03-Aug-27
P3140	Install New Light Cans & Sign Bases	1d	04-Aug-27	04-Aug-27
P3150	Install 867E Junction Can	2d	04-Aug-27	05-Aug-27
P3160	Place Back & Roll Casper Rock	2d	04-Aug-27	05-Aug-27
P3170	Pull Wire	2d	06-Aug-27	09-Aug-27
P3180	Install Lights & Guidance Signs	2d	10-Aug-27	11-Aug-27
P3190	Temp Pavement Markings	4d	12-Aug-27	17-Aug-27
Closeout		32d	04-Aug-27	17-Sep-27
A3040	Waiting Period	30d	04-Aug-27	02-Sep-27
c1230	Substantial Completion	0d		17-Aug-27
A3000	Demobilization	10d	18-Aug-27	31-Aug-27
A3010	Project Closeout	22d	18-Aug-27	17-Sep-27
A3020	Install Final Striping	4d	03-Sep-27	09-Sep-27

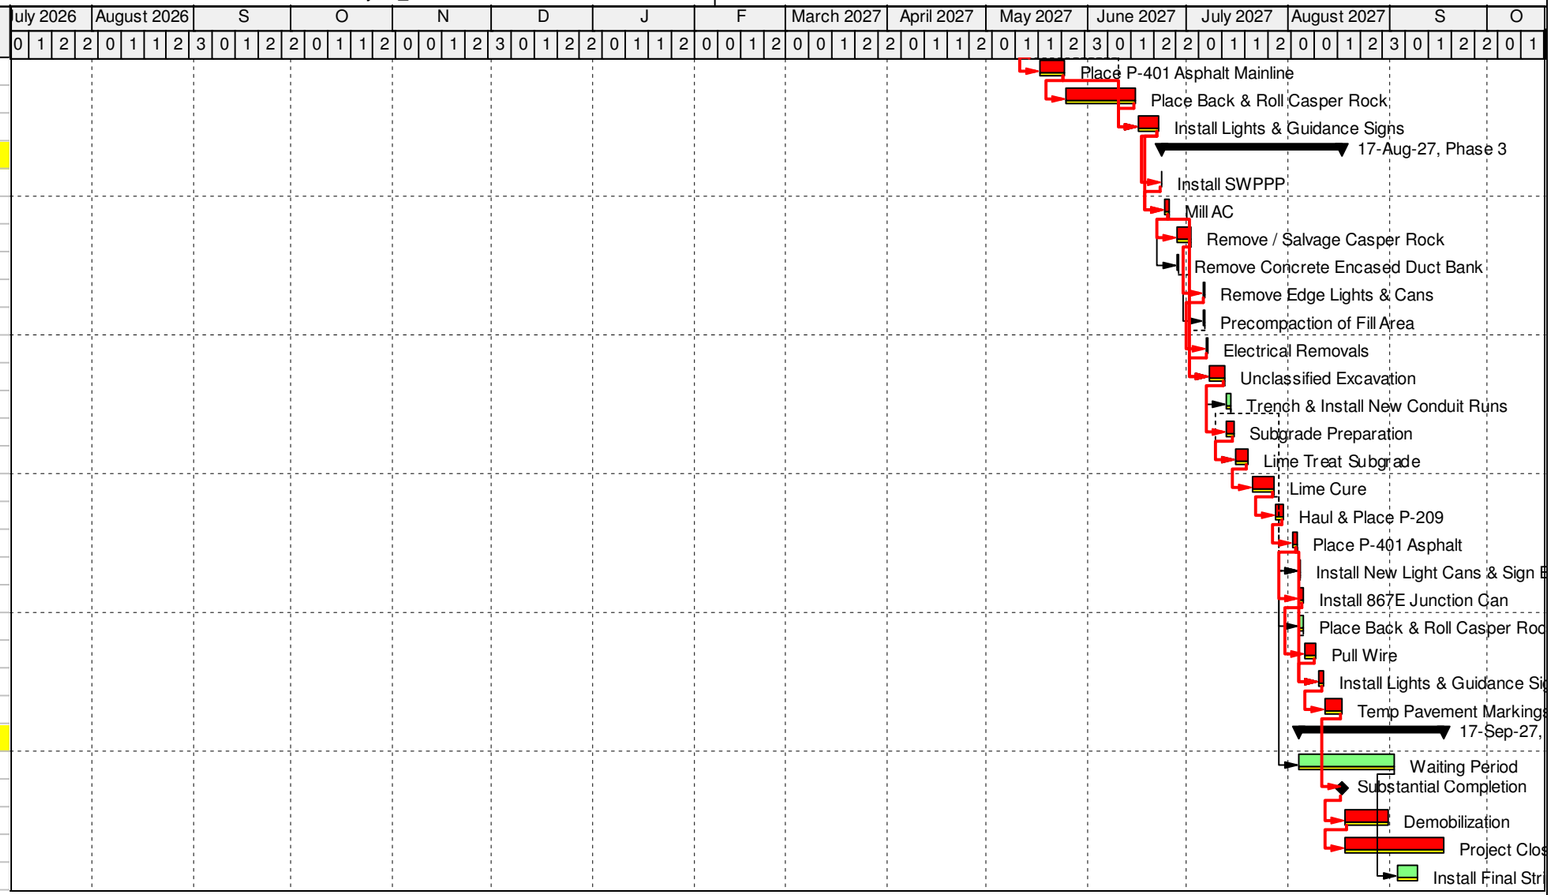

Project Baseline Bar
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

© Oracle Corporation
